

Grouting Instruction VL4 FIRST GROUT FAN

Tunnel	VL4 (W=6,9-H=6,9)
Instruction N°	572

Chainage	1+191,1
Total Inflow face	
Total Inflow Probe hole	3 4/5
Water pressure measured	6 bar

Mark additional holes with x and number

Erase holes not to be used

1- DRILL HOLES: 1 TO 15 WITH ANGLE 15°

PRIMARY ROUND: 2,8,14,6,12,4,10,15 AND GROUT

SECONDARY ROUND: 1,7,13,5,11,3,9 AND GROUT

2- DRILL HOLES IN ORDER: 17,19,21,18,20,16
PARALLEL TO THE TUNNEL AND GROUT.

THE PACKER SHOULD BE INSTALLED BETWEEN 1,5
AND 3,0 M (DEPENDING OF ROCK MASS
CONDITION, REF LEAKAGE)

Design Mix (Type A,B,C, D or E)	A
---------------------------------	---

WCR	0,65
-----	------

Closure criteria


Pmax	25*
Vmax (l/m borehole)	85
GIN	1000

*IF GROUNDWATER PRESSURE IS
HIGHER THAN 10 BAR THEN APPLY
GROUT PRESSURE OF 2,5 TIMES
GROUNDWATER PRESSURE

Instructed by:	ERNESTO HENRIQUEZ JARA
Instruction date:	25-07-16

	HOLES 1-15	16-21
N° of Grout holes	15	6
Grout holes length (m)	24	24
Grout hole angle ref Tunnel axis	15	0

Position of Grout holes 1st grout round:

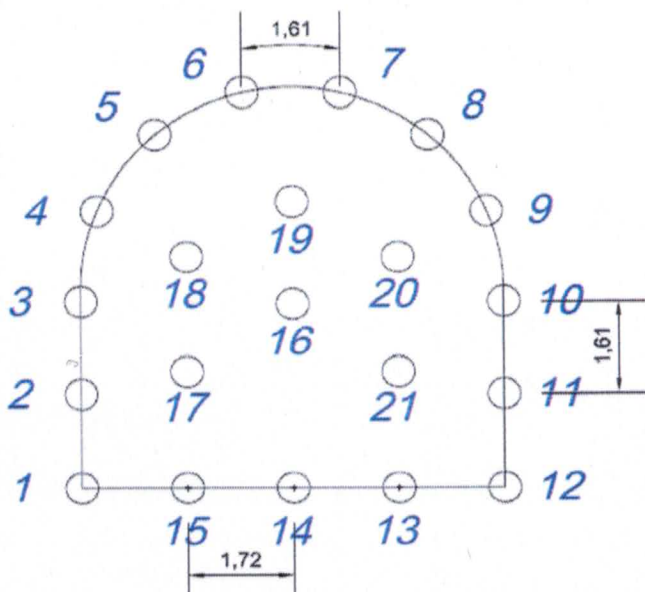

NOTES:

- 1-DRILL GROUTING HOLES TO THE FULL DEPTH AS INSTRUCTED, EVEN WITH SIGNIFICANT DISCHARGE (>2.5 l/sec)
- 2- THE MAXIMUM INCREASE OF GROUTING PRESSURE SHALL BE NOT MORE THAN 2,5 BAR PER MINUTE.
- 3- DRY HOLE SHALL NOT BE REDRILLED OR REGROUTED.

STRABAG

M. Rosenfeld

Name

R. M.

Signature

SAM

ERNESTO HENRIQUEZ JARA

Name

[Signature]

Signature
